

PASS Article 13 / SME Program Report

Date of Update: 3/10/2016

Program Name: TAMR (STARS/CARTS)

Program Contact/s: See Attachment, Read-Out Structure 2016Mar09.pdf

Current Program Status:

See Attachment, Status of Activities for FY16 IOCs 2016Mar09.pdf

TAMR Phase 1 – Tech Refresh (G1/G2 to G4): A90/BCT (Boston Consolidated TRACON), Shakedown Phase 1 completed, Shakedown Phase 2 and IOC scheduled for Apr 2016.

TAMR Phase 1 – Facilities Projects: L30 (Las Vegas) TRACON, Shakedown Phase 1 currently in progress. PBI (West Palm Beach), Shakedown Phase 1 completed.

TAMR Phase 3 Segment 1 – ARTS IIIE to G4: 9 of 11 ARTS IIIE have achieved IOC on STARS G4, next site to IOC is C90, scheduled for 4/6/2016.

TAMR Phase 3 Segment 2 – ARTS IIE to STARS ELITE: 16 of 91 ARTS IIE have achieved IOC on STARS ELITE, next sites to IOC are ACY (Atlantic City) 3/11/2016, CHA (Chattanooga) 3/14/2016, and GPT (Gulfport) 3/18/2016,

Issues Affecting PASS: None at this moment.

Program Issues: None at this moment.

Identify Support Needs: None at this moment.

Other: Nothing to report at this moment


Documentation Attached: TAMR Key Milestone 30 Day Look-Ahead 2016Mar09.pdf, Read-Out Structure 2016Mar09.pdf, Status of Activities for FY16 IOCs 2016Mar09.pdf

TAMR Key Milestone 30 Day Look-Ahead

Segment	Location Identifier	Activity Name	P/A Start	P/A Finish
S2	GGG	Joint Site Survey	3/1/2016	3/4/2016
S2	FAY	Joint Site Survey	3/2/2016	3/5/2016
S2	AVP	Equipment Delivery	3/8/2016	3/8/2016
S2	ACY	IOC	3/11/2016	3/11/2016
S1	PCT.OPS	IOC Event 3 - Optiional ConOps	3/13/2016	3/13/2016
S2	CHA	IOC (WWG Coordinated Date)	3/14/2016	3/14/2016
S2	HUF	Initial Site Survey	3/15/2016	3/17/2016
S2	TRI	Initial Site Survey	3/15/2016	3/17/2016
Phase 1	PIT	Joint Site Survey	3/15/2016	3/18/2016
Phase 1.F	TUS	Equipment Delivery (Remaining equipment delivered)	3/15/2016	3/15/2016
S2	SUX	Joint Site Survey	3/16/2016	3/19/2016
Phase 1	TUL	Initial Site Survey (Kick Off Telecon)	3/17/2016	3/17/2016
Phase 1.F	TUS	CAI	3/17/2016	3/17/2016
S2	GPT	IOC	3/18/2016	3/18/2016
S1	PCT.OPS	IOC Event 4 - Optional	3/20/2016	3/20/2016
S2	ROW	Equipment Delivery	3/22/2016	3/22/2016



Status of Activities for FY16 IOCs

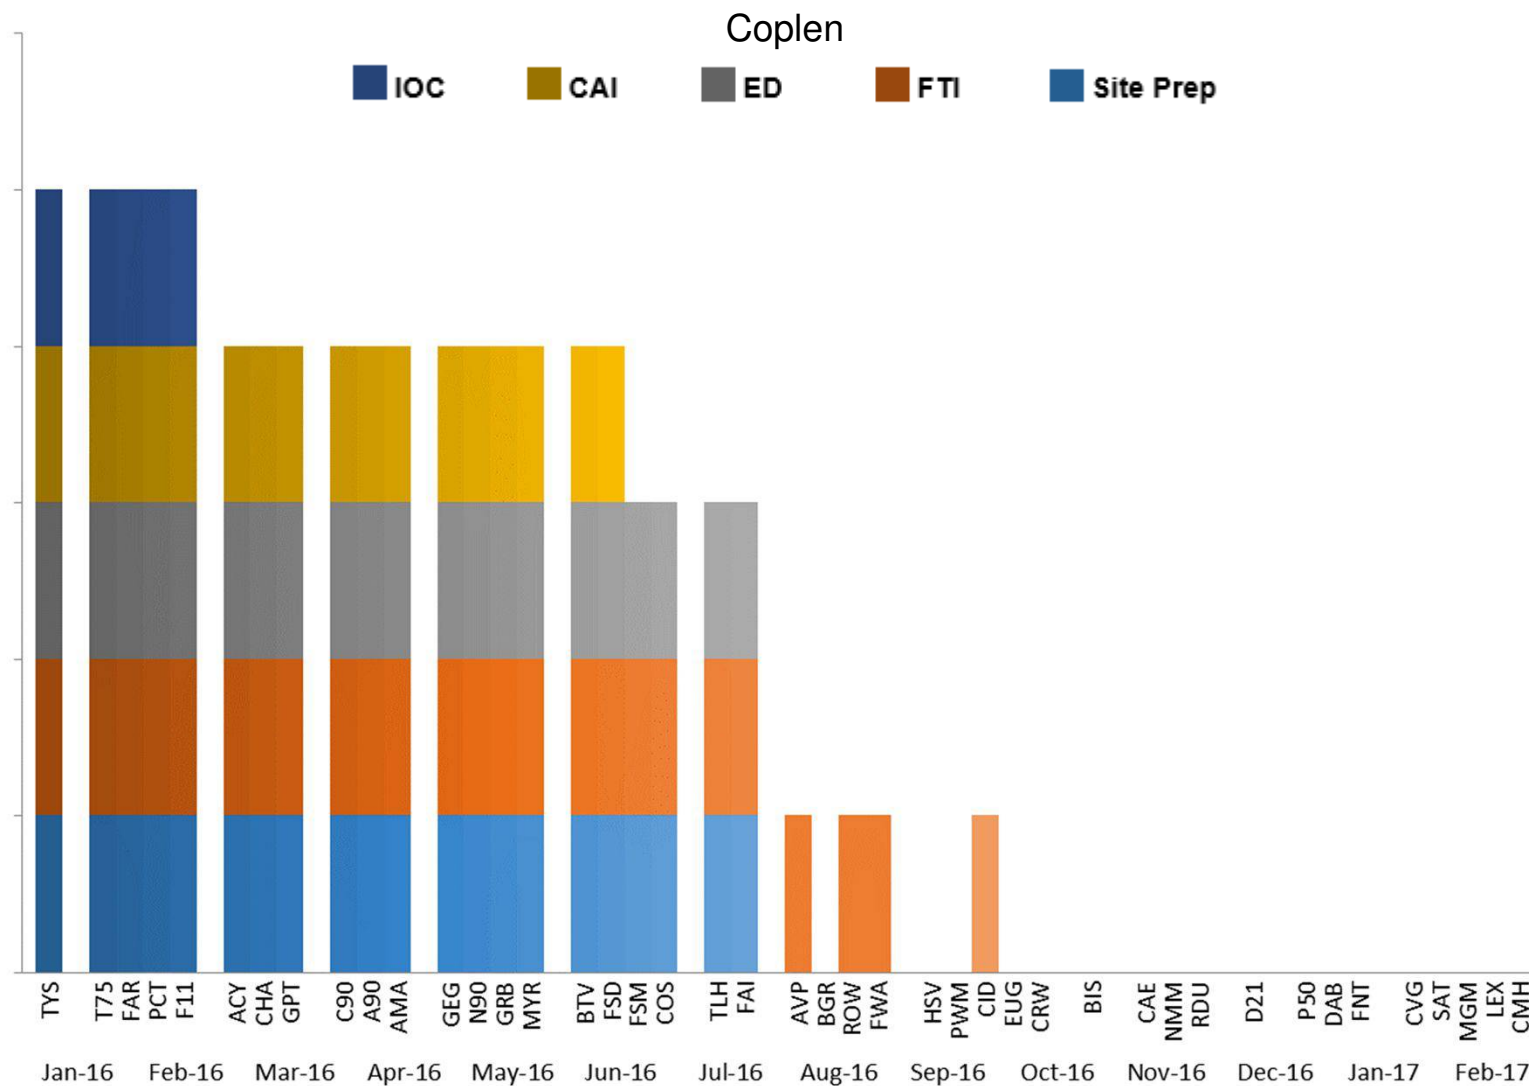

*DoD and facilities sites not included



Read-Out Structure

- **Program Management: Lisa Bercher**
- **Deputy Program Management: Juanita Kennedy**

- **Implementation Manager: Kim Coplen**
 - Phase 1 Deployment: Adrienne Baier
 - Phase 3 Segment 1 Deployment: Amber Natale
 - Phase 3 Segment 2 Deployment: Renee Putsche
 - Logistics: Daren Magness
 - Training: Art Hutchinson
- **System Engineer Manager: Gian Burdhimo**
 - Software Development: Tony D'Avella
 - Externally Funded Capabilities: Susan MacKeen
 - Testing: Steve Frith, Ed Gaguski
 - System Engineering/Hardware: Gian Burdhimo
- **Program Control Manager: Jeffery Hobbs**
 - Business Management: Quiana Shaw
 - Risk Management: Megan Wolterman
 - CRDL Status: Phyllis Bell
